

Construction Portfolio Financial Tracker - Power BI Dashboard

Portfolio Case Study

Valeriia Evtushenko

Budget vs. Actual Analysis / Risk Monitoring / Completion Tracking

Model Objectives & Key Questions

This dashboard is designed to monitor and manage construction portfolio performance across multiple regions.

- 1. WHICH PROJECTS ARE EXCEEDING THEIR BUDGETS?**
(Focus: Cost control and budget utilization)
- 2. HOW MUCH BUDGET REMAINS AFTER COMMITTED COSTS?**
(Focus: Liquidity and available funding)
- 3. WHICH PROJECTS ARE AT RISK OF COST OVERRUN?**
(Focus: Risk identification and mitigation)

Outcome: The dashboard provides actionable insights through interactive visualisations, budget tracking features, and color—coded risk flags to monitor project financial health.

Project Portfolio Overview

9M

Contracted Budget

7M

Actual Costs

865K

Committed Costs

983K



Remaining Budget

80.07%

Budget Utilization %

73.40

Average of Completion %

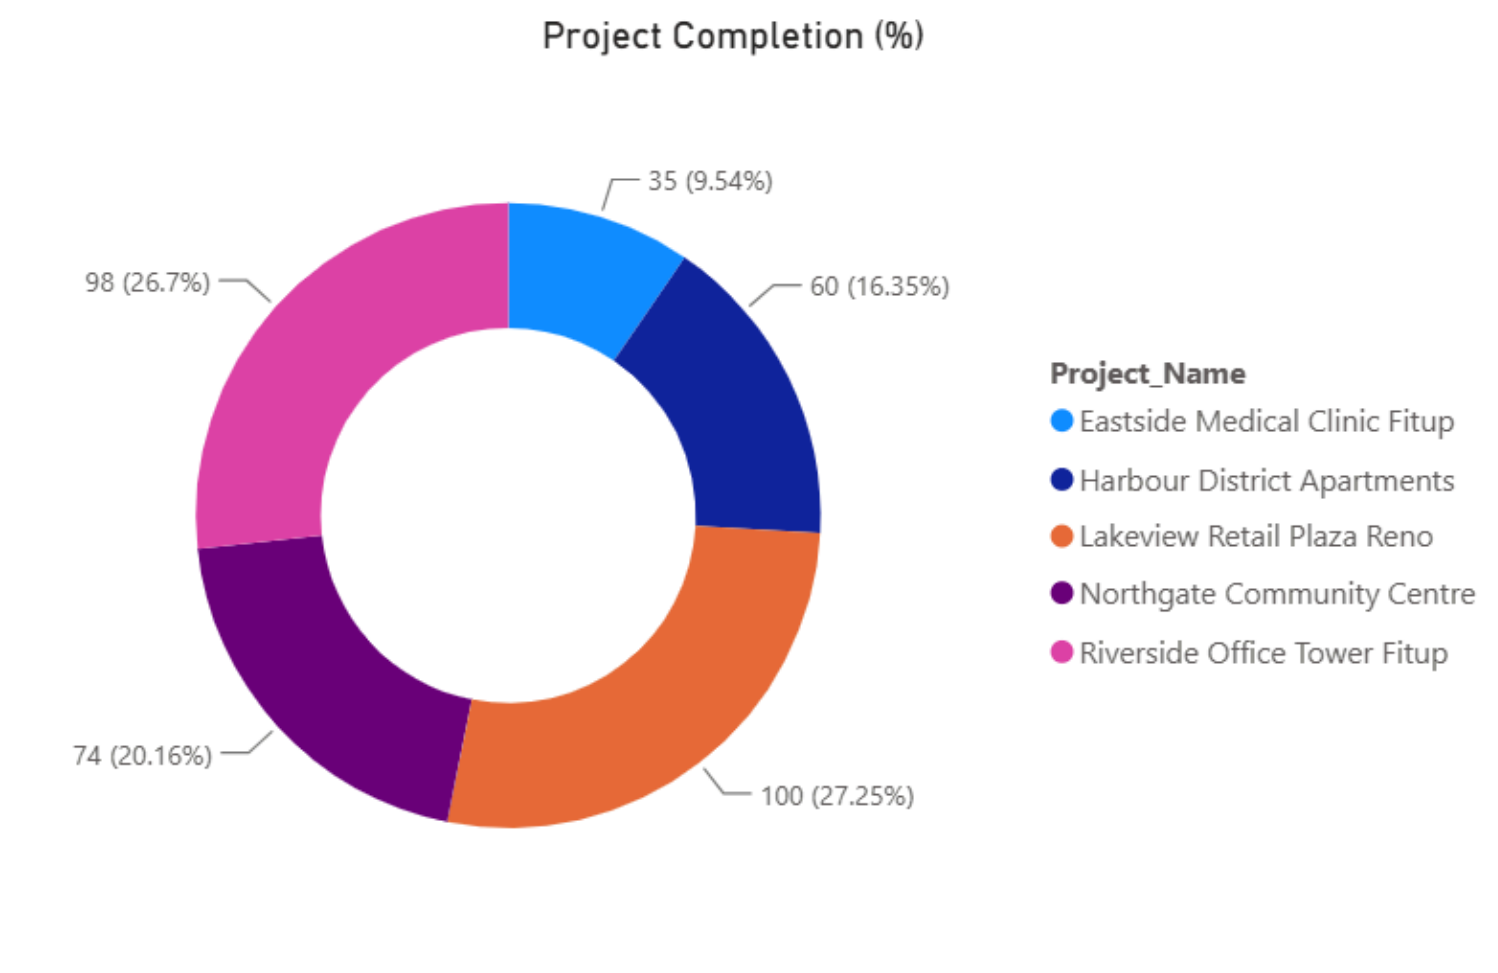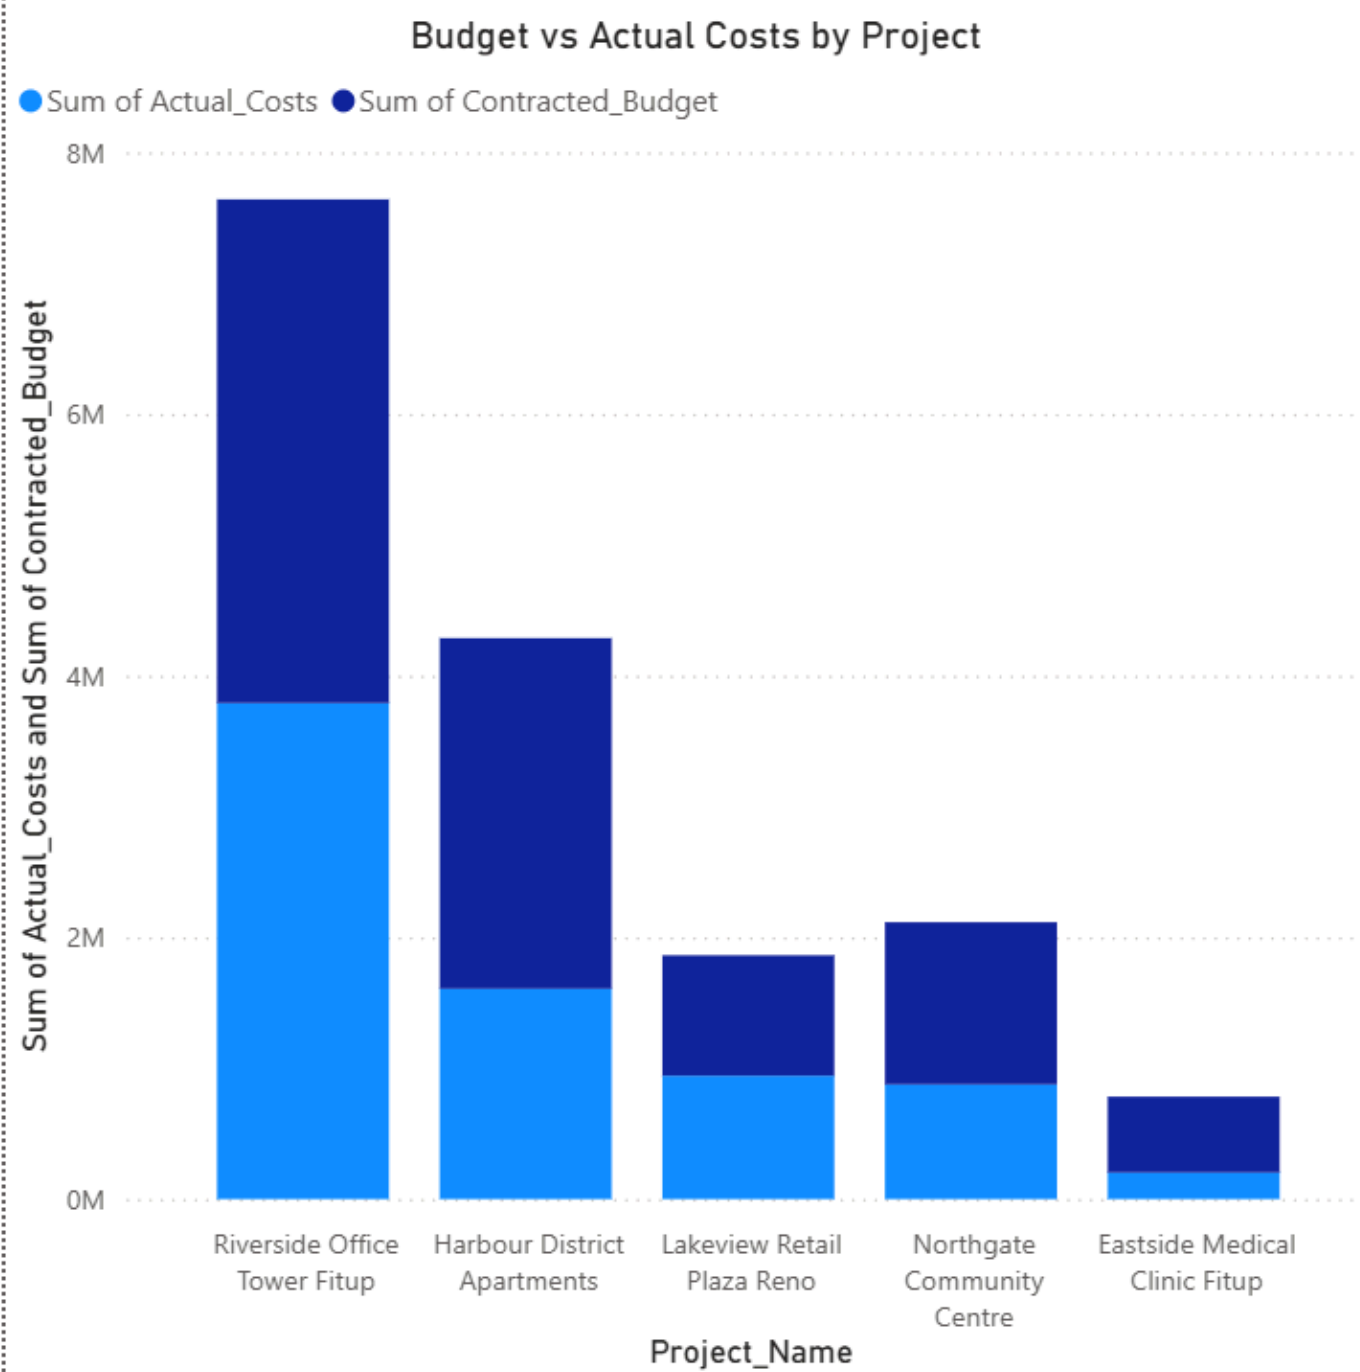

Project Status & Variance Summary			
Project_Name	Status	Variance_Amount	Completion_Pct
Lakeview Retail Plaza Reno	Completed	-23600	100
Eastside Medical Clinic Fitup	In Progress	232000	35
Harbour District Apartments	In Progress	536000	60
Northgate Community Centre	In Progress	221500	74
Riverside Office Tower Fitup	In Progress	16800	98

Key Conclusions

1. Budget Utilization vs. Completion: the portfolio has spent ~80% of its contracted budget but is only ~74% physically complete on average — a gap worth monitoring, since it means cost is running slightly ahead of progress overall.
2. Cost Overruns: 1 project over budget (Lakeview Retail Plaza Reno), already completed.
3. Risk Flags: projects with variance > \$200K require management attention.
4. Best Cost-to-Progress Match: Harbour District Apartments and Riverside Office Tower Fitup show budget usage closely tracking physical completion, despite Harbour carrying the largest dollar variance in the portfolio.
5. Monthly trend: Lakeview Retail Plaza Reno is the only project running over its monthly budget in every month tracked (Jan–Jun 2025), consistent with its overall over-budget completion.

**Proactive cost management across all regions
is critical to portfolio sustainability**

Thank you for your time!

I'm open to new opportunities in Financial Analysis / FP&A

Valeriia Evtushenko
[linkedin.com/in/valeriia-evtushenko-51110a304](https://www.linkedin.com/in/valeriia-evtushenko-51110a304)
